


2010 SAME Blue Ridge Post Challenges of Contingency Contracting

COL Steven Roemhildt

Deputy Commander (Main)

Transatlantic Division

18 February 2010



US Army Corps of Engineers
BUILDING STRONG®



BUILDING STRONG!

What is USACE ?

HQ

FY09 Military Program

\$ 27.7 B (inc. Stimulus)

12,000 personnel

Military Construction

Contingency Operations
Installation Support

International and
Interagency Support

**Engineer
Commands**

FY09 Civil Works Program

\$ 15.6 B (inc. Stimulus)

25,000 personnel

Navigation

Hydropower

Flood Damage Reduction

Shore Protection

Water Supply

Regulatory

Recreation

9 Divisions

(Direct Funded)

45 Districts

(Project Funded)

Homeland Security

Environmental

Real Estate

**Private
Industry
Partners**

Engineer Research and Development Center
\$ 1 BIL @ Seven (7) diverse research laboratories

USACE Global Engagement


- Countries – 100+
- *USACE/USAID engagement since 1998*
- * *USACE/MCC engagement*

ARCTIC




What is USACE?

Private Industry Partnerships

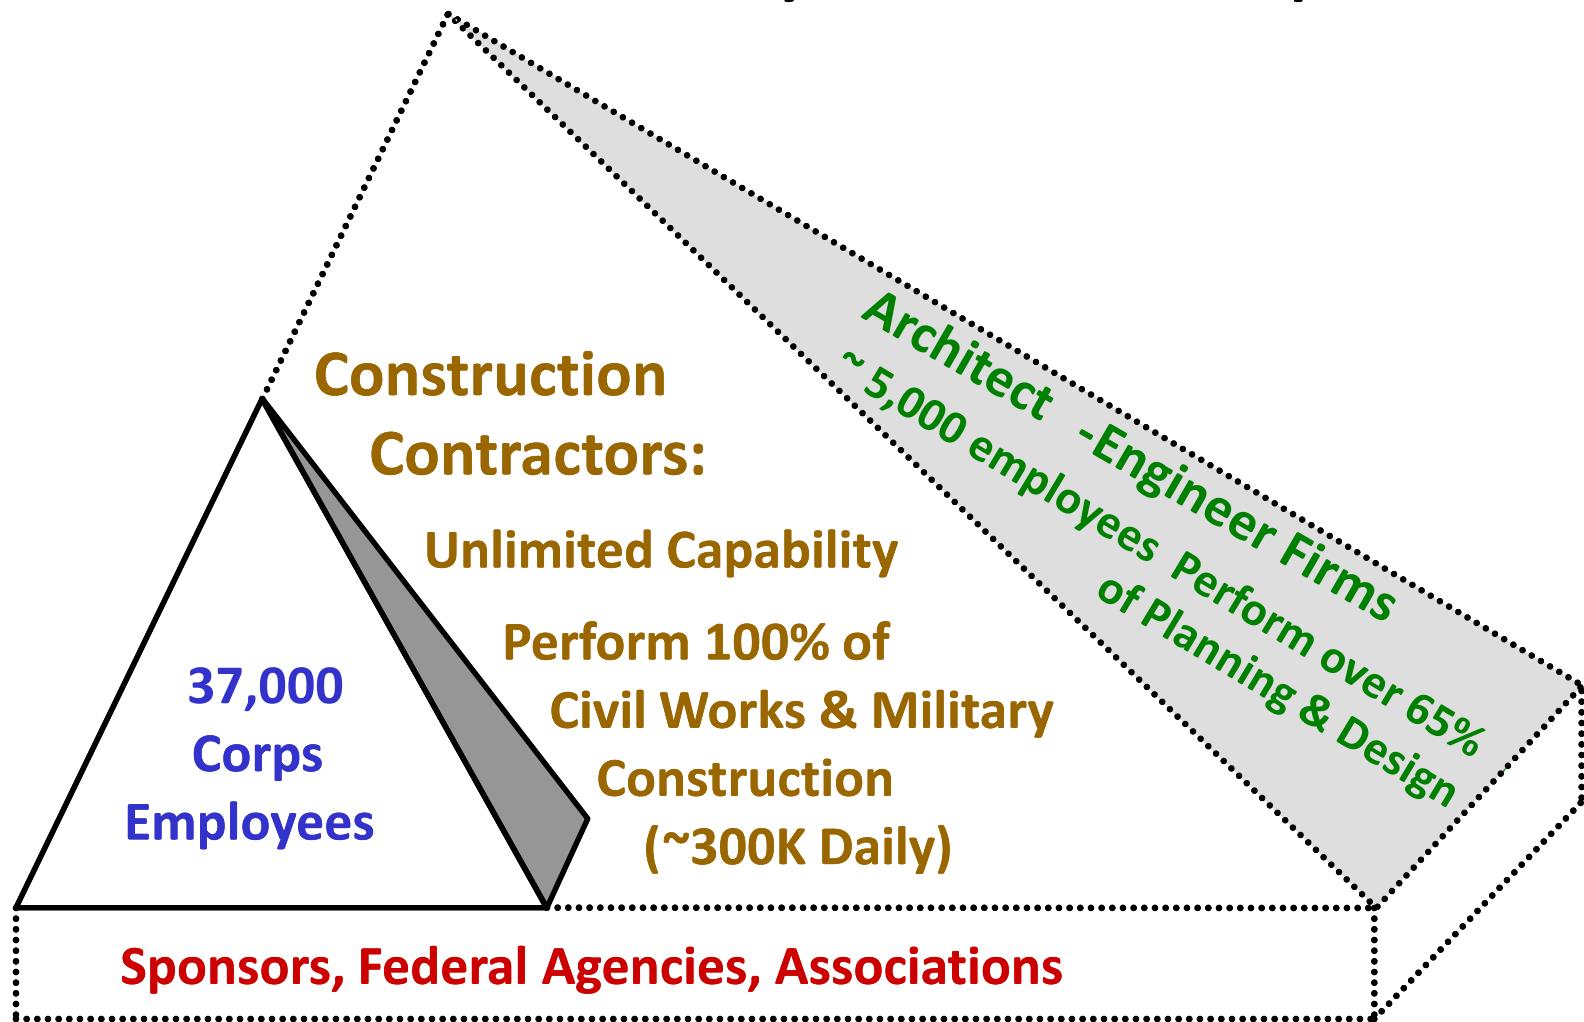

Where We Are...

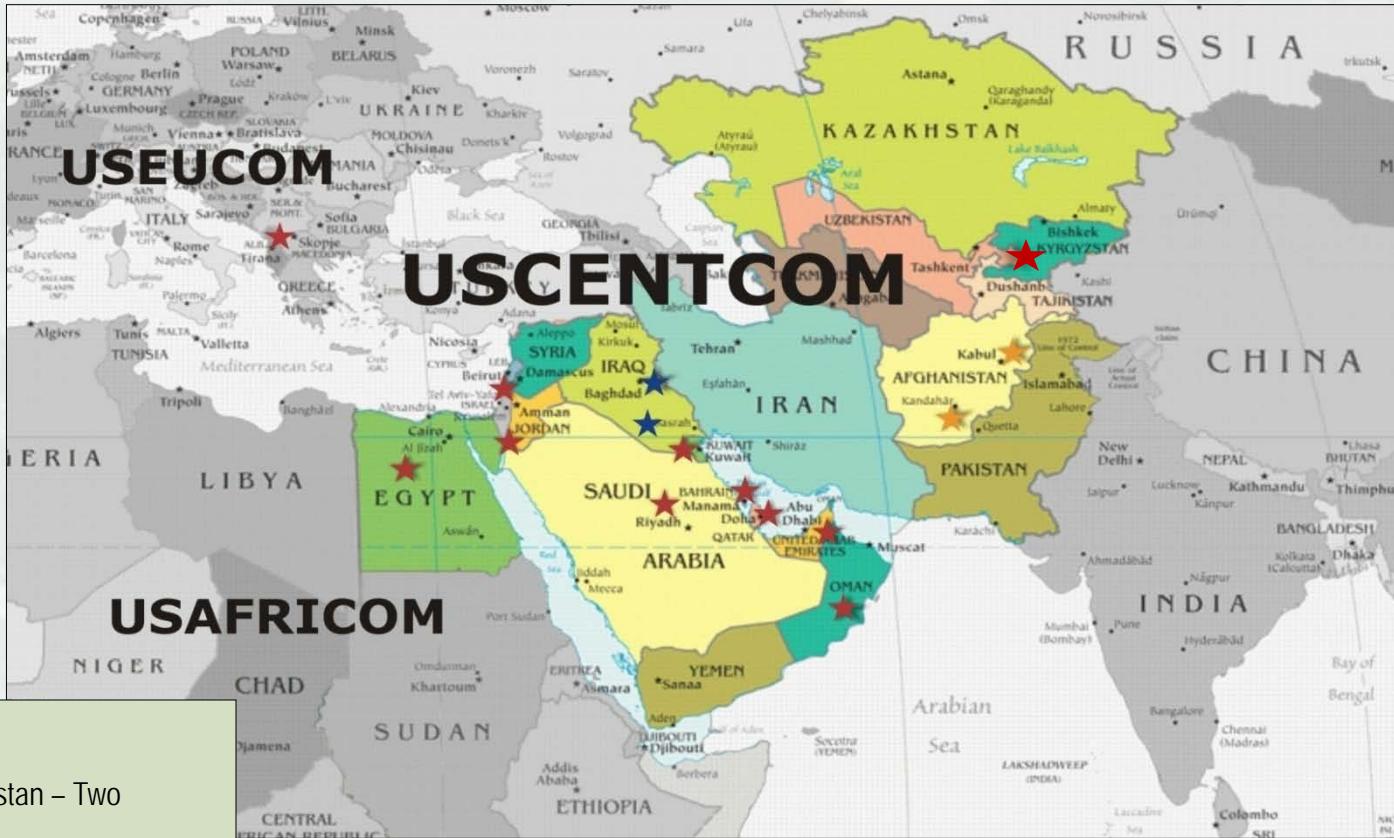


Legend

- ★ Afghanistan – Two Districts
- ★ Iraq – Two Districts
- ★ Middle East District



BUILDING STRONG®

Transatlantic Division Programs

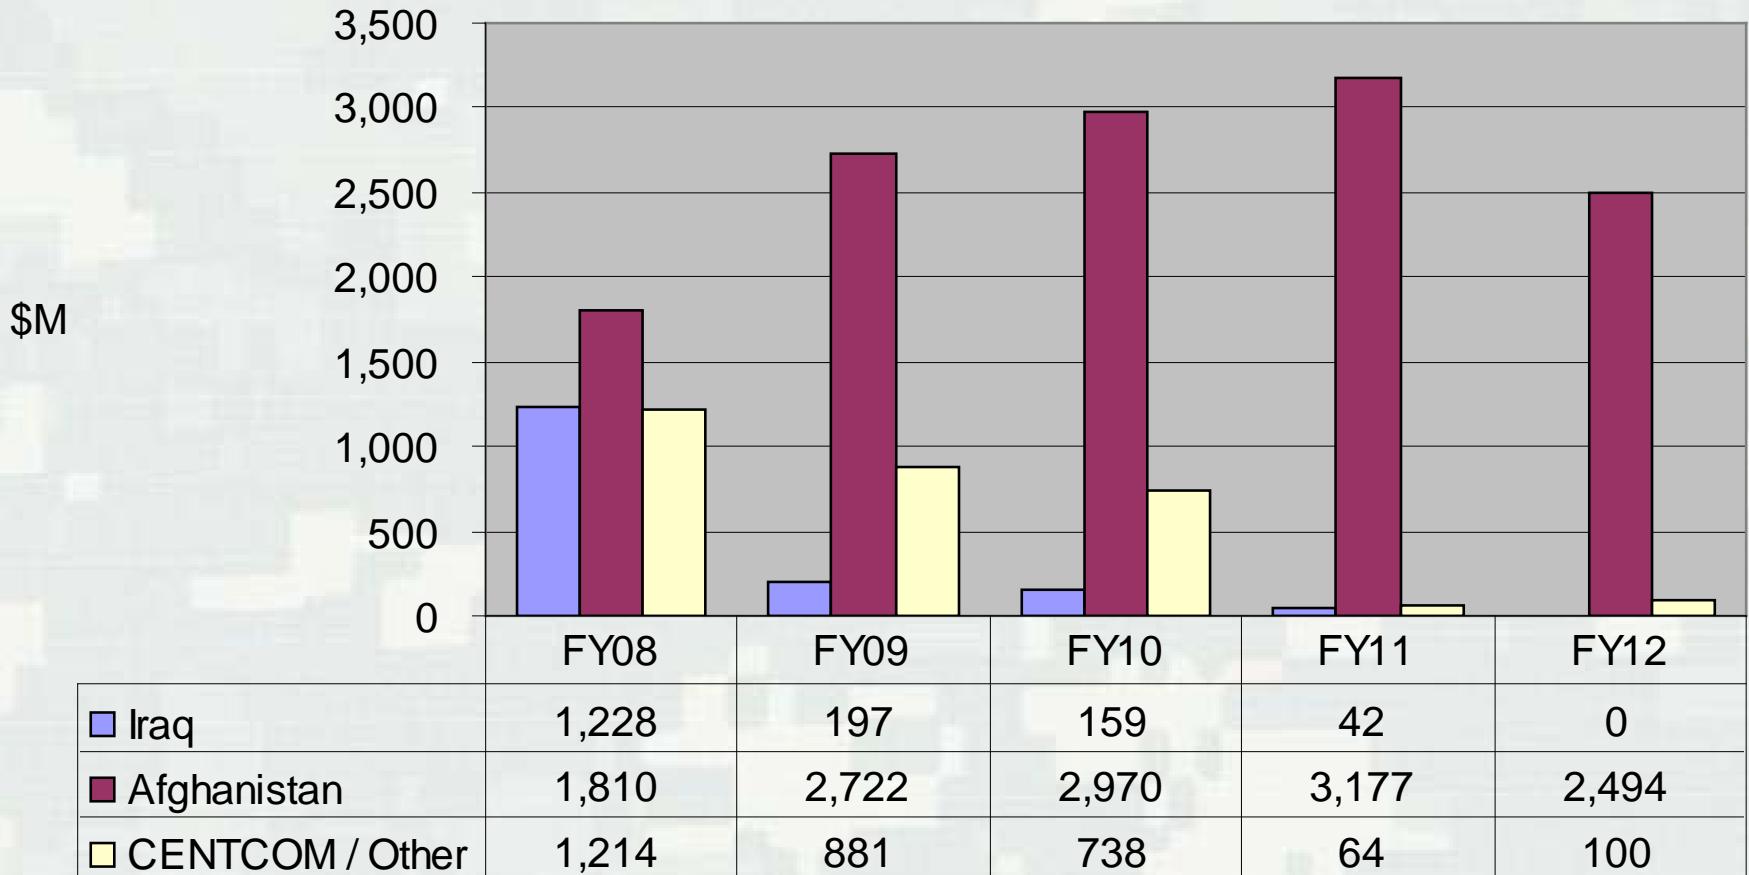

TAD Mission

The Transatlantic Division provides design and construction execution services to CENTCOM and related engineering services to designated activities within the CENTCOM area of responsibility to establish the conditions for regional security, stability, and prosperity; provides command and control, engineering services and deployment support for USACE world-wide contingency operations.




TAD METL


- Provide command and control for Transatlantic Districts
 - ▶ Operate a Regional Business Center that provides regional governance
 - ▶ Manage Division reach back support between forward deployed Districts and CONUS support
 - ▶ Provide a quality assurance program aligned with the PMBP business process
 - ▶ Provide CENTCOM unity of command and unity of effort for all USACE elements
 - ▶ Interface with other non-CENTCOM agencies/organizations to match capabilities with emerging requirements
- Plan and execute a Military Construction and International & Interagency Service (IIS) program
 - ▶ Plan, design, construct, and deliver Military Construction projects
 - ▶ Plan, design and execute IIS programs
 - ▶ Maintain expertise in developing and executing the FMS program
 - ▶ Provide real estate support to DoD & DoS organizations
 - ▶ Support facility management in CENTCOM AOR as requested
- Respond to and support USACE contingency operations
 - ▶ Support the establishment of engineer contingency elements as directed
 - ▶ Operate UDC for contingency ops & provide RSOI support as necessary
- Maintain a workforce capable of meeting peacetime, emergency, and contingency requirements
 - ▶ Provide general and administrative support services
 - ▶ Provide human resource support
 - ▶ Provide legal services
 - ▶ Provide military personnel administrative support
 - ▶ Manage a training program



Transatlantic Division

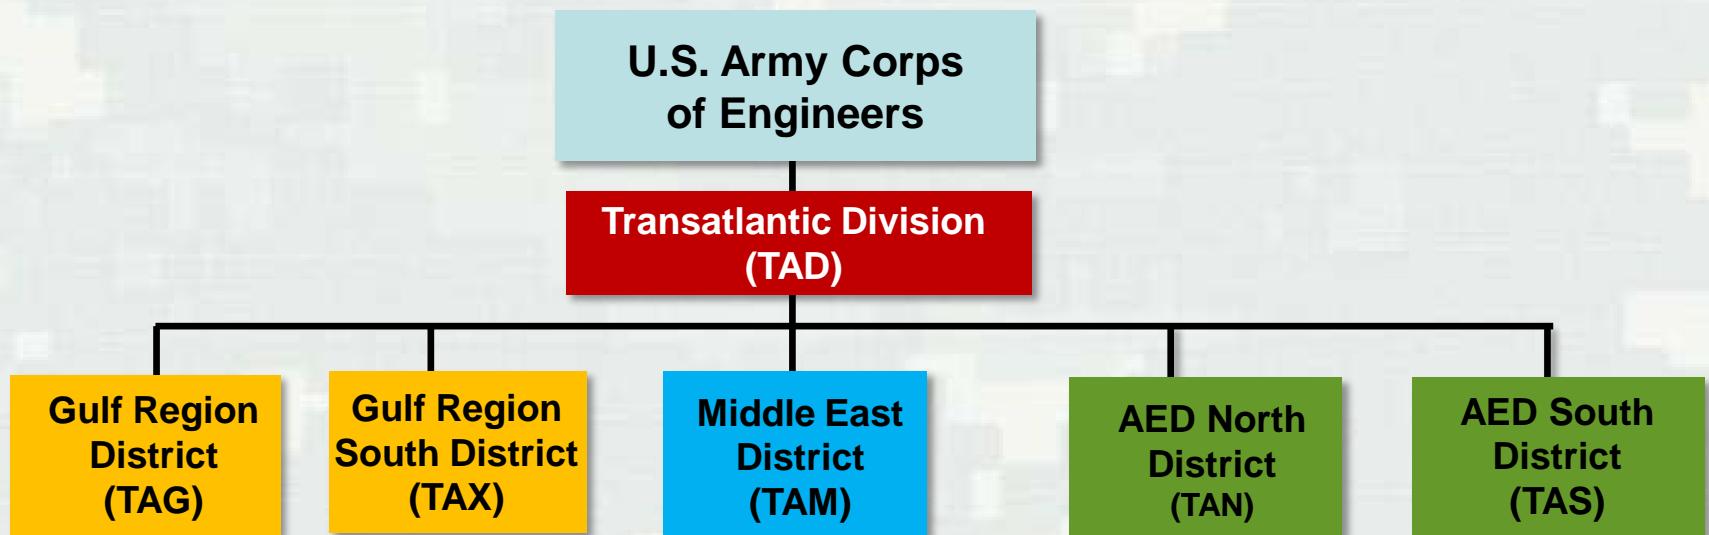

Overall TAD C2 concept

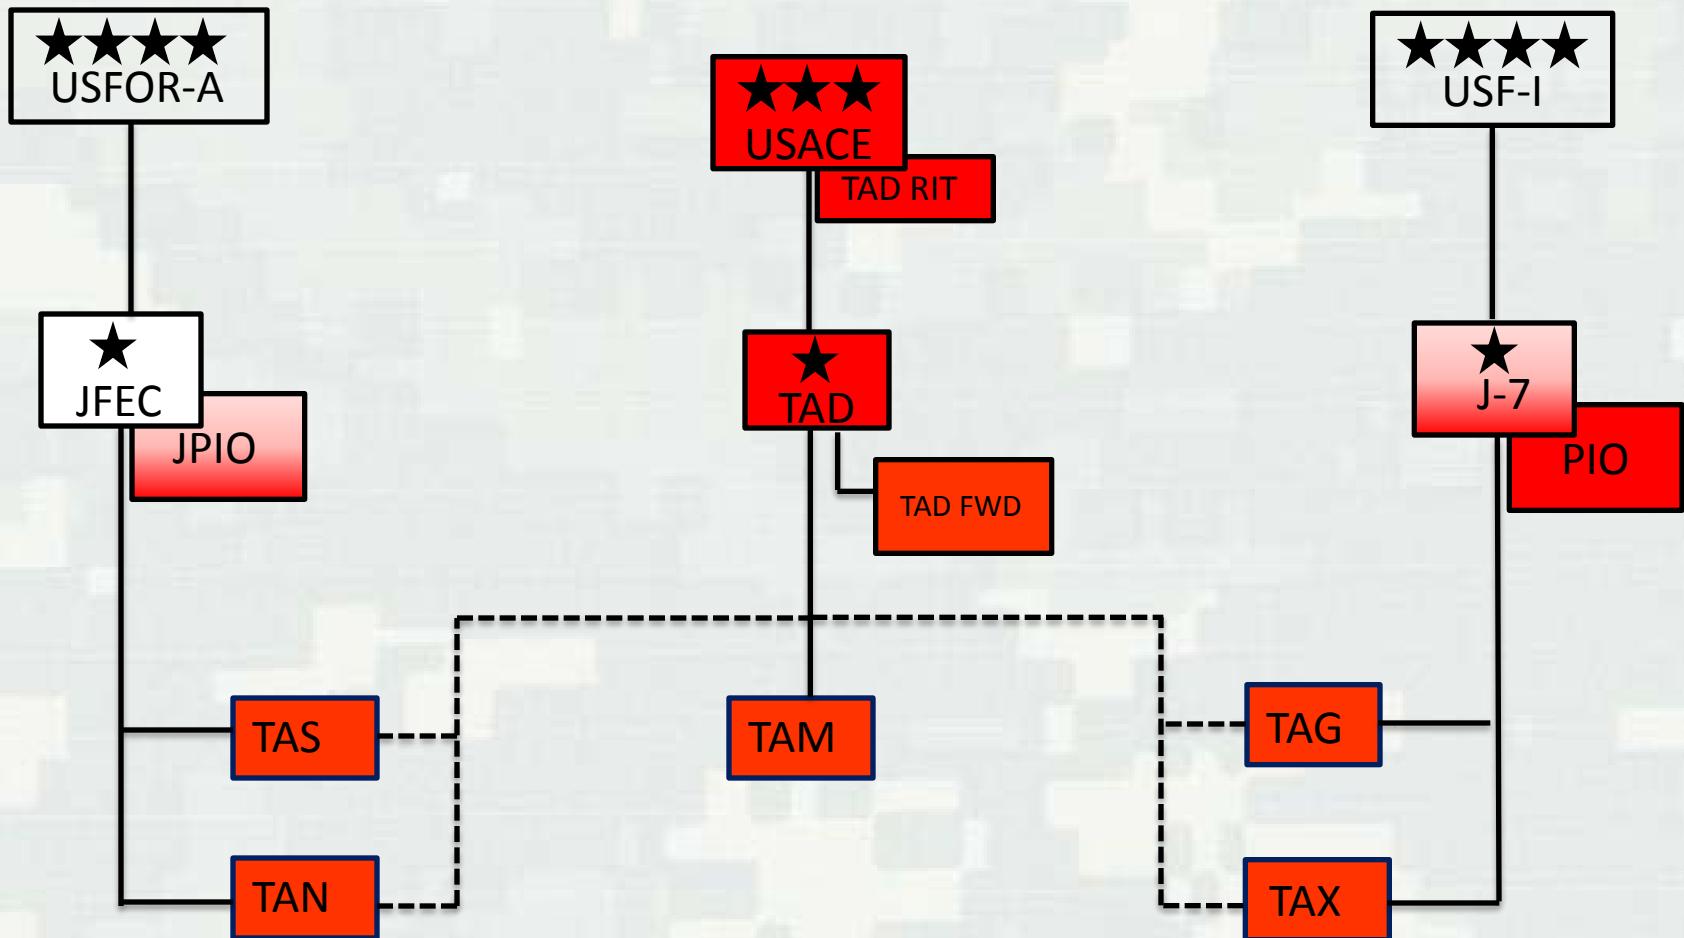

Assigned or TACON
Admin, resource, and policy support

Customer/Stakeholders

- US Central Command and component services
- Department of Defense agencies
- Other US government agencies
- Foreign military forces and foreign organizations
- US Army Europe



BUILDING STRONG®

Engineering & Construction Mission

– Types of Work

Middle East District:

Air field pavement

Warehouses

Administrative Facilities

Barracks

Dining Facilities

Iraq:

Roads

Water Treatment Facilities

Afghanistan:

Roads

Bridges

Airfield Pavements

Administrative Facilities

Barracks

Dining Facilities

Medical Facilities

Water & Waste Treatment

Police Stations


Border Forts

Warehouses


Power Generation



AED Area of Responsibility

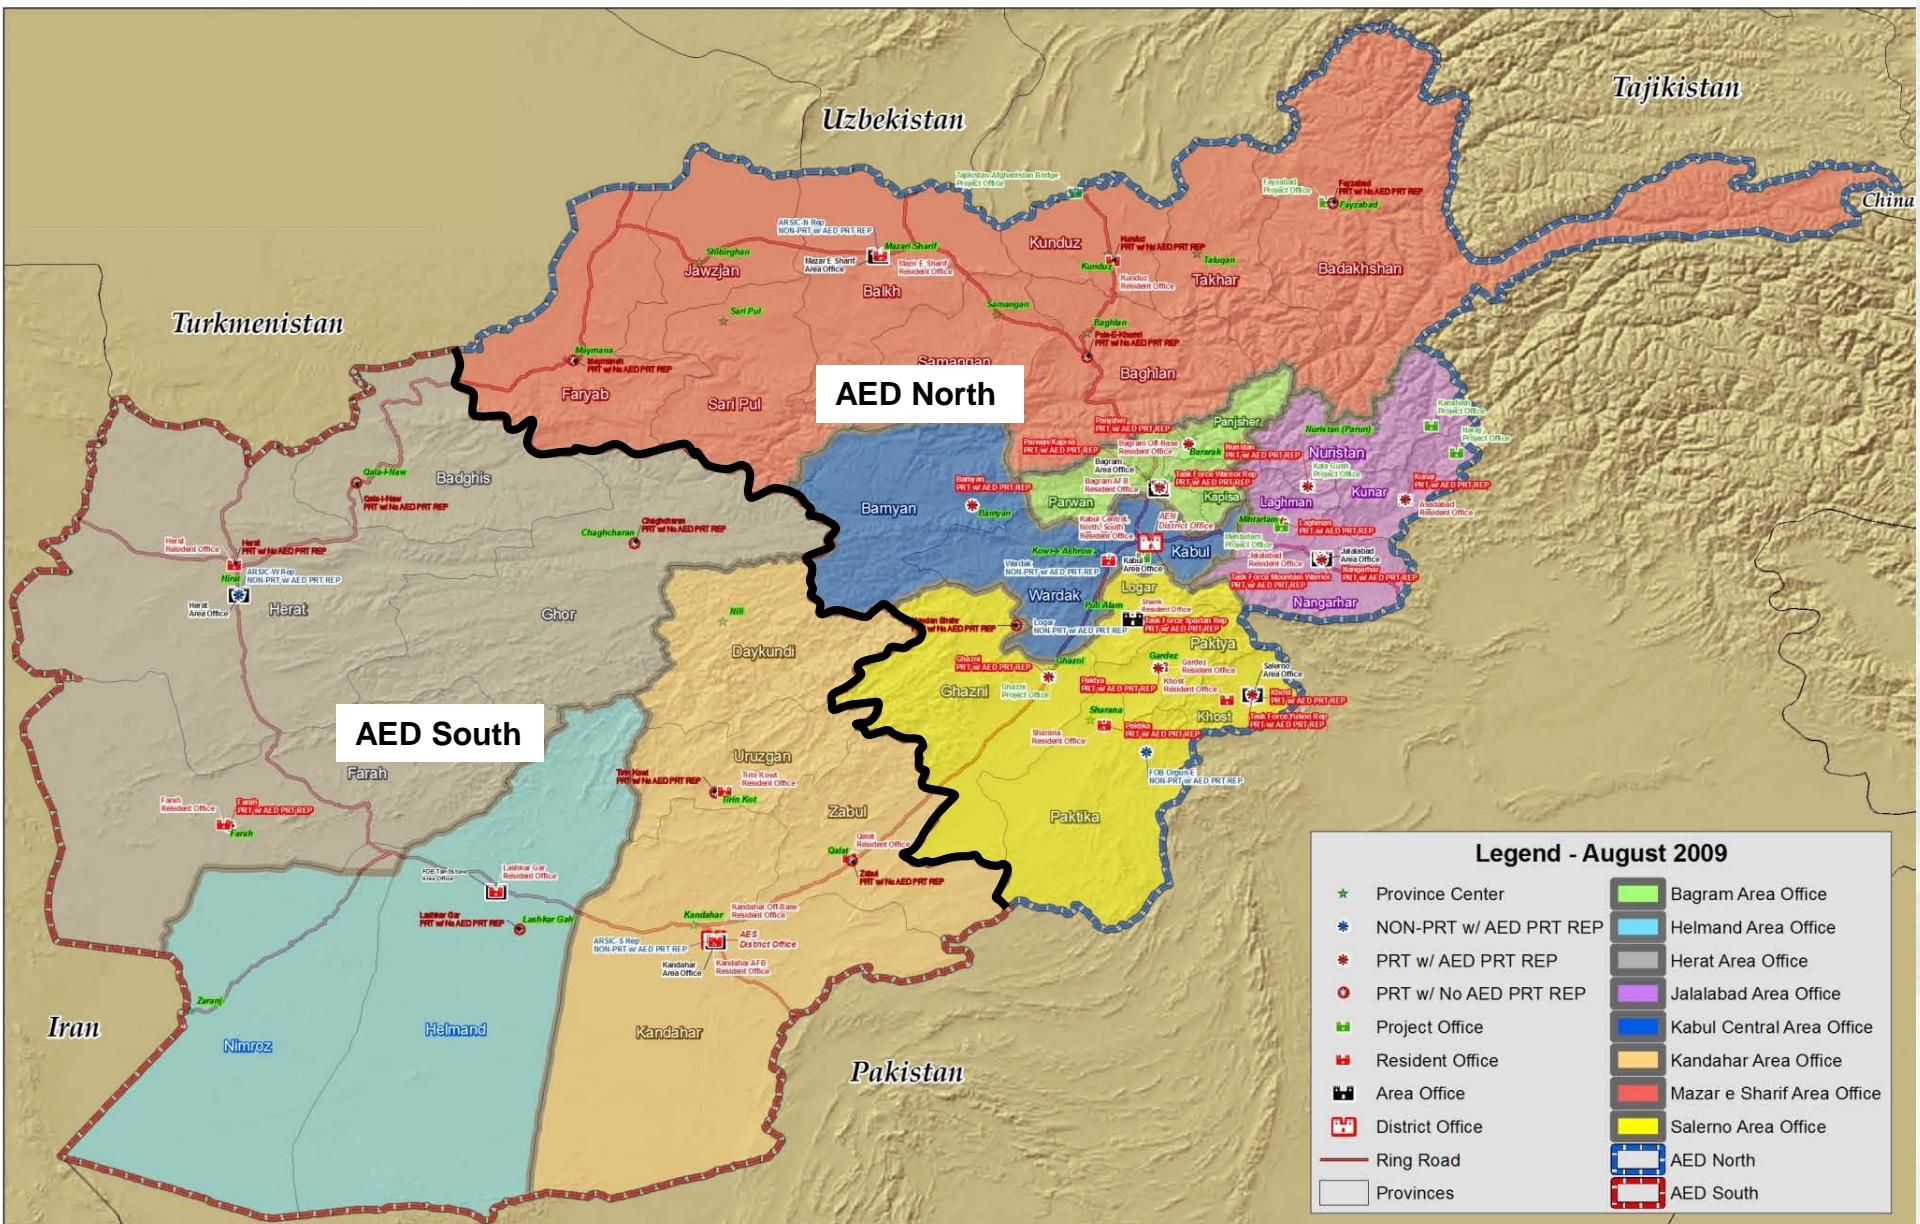

AED Workload Projections

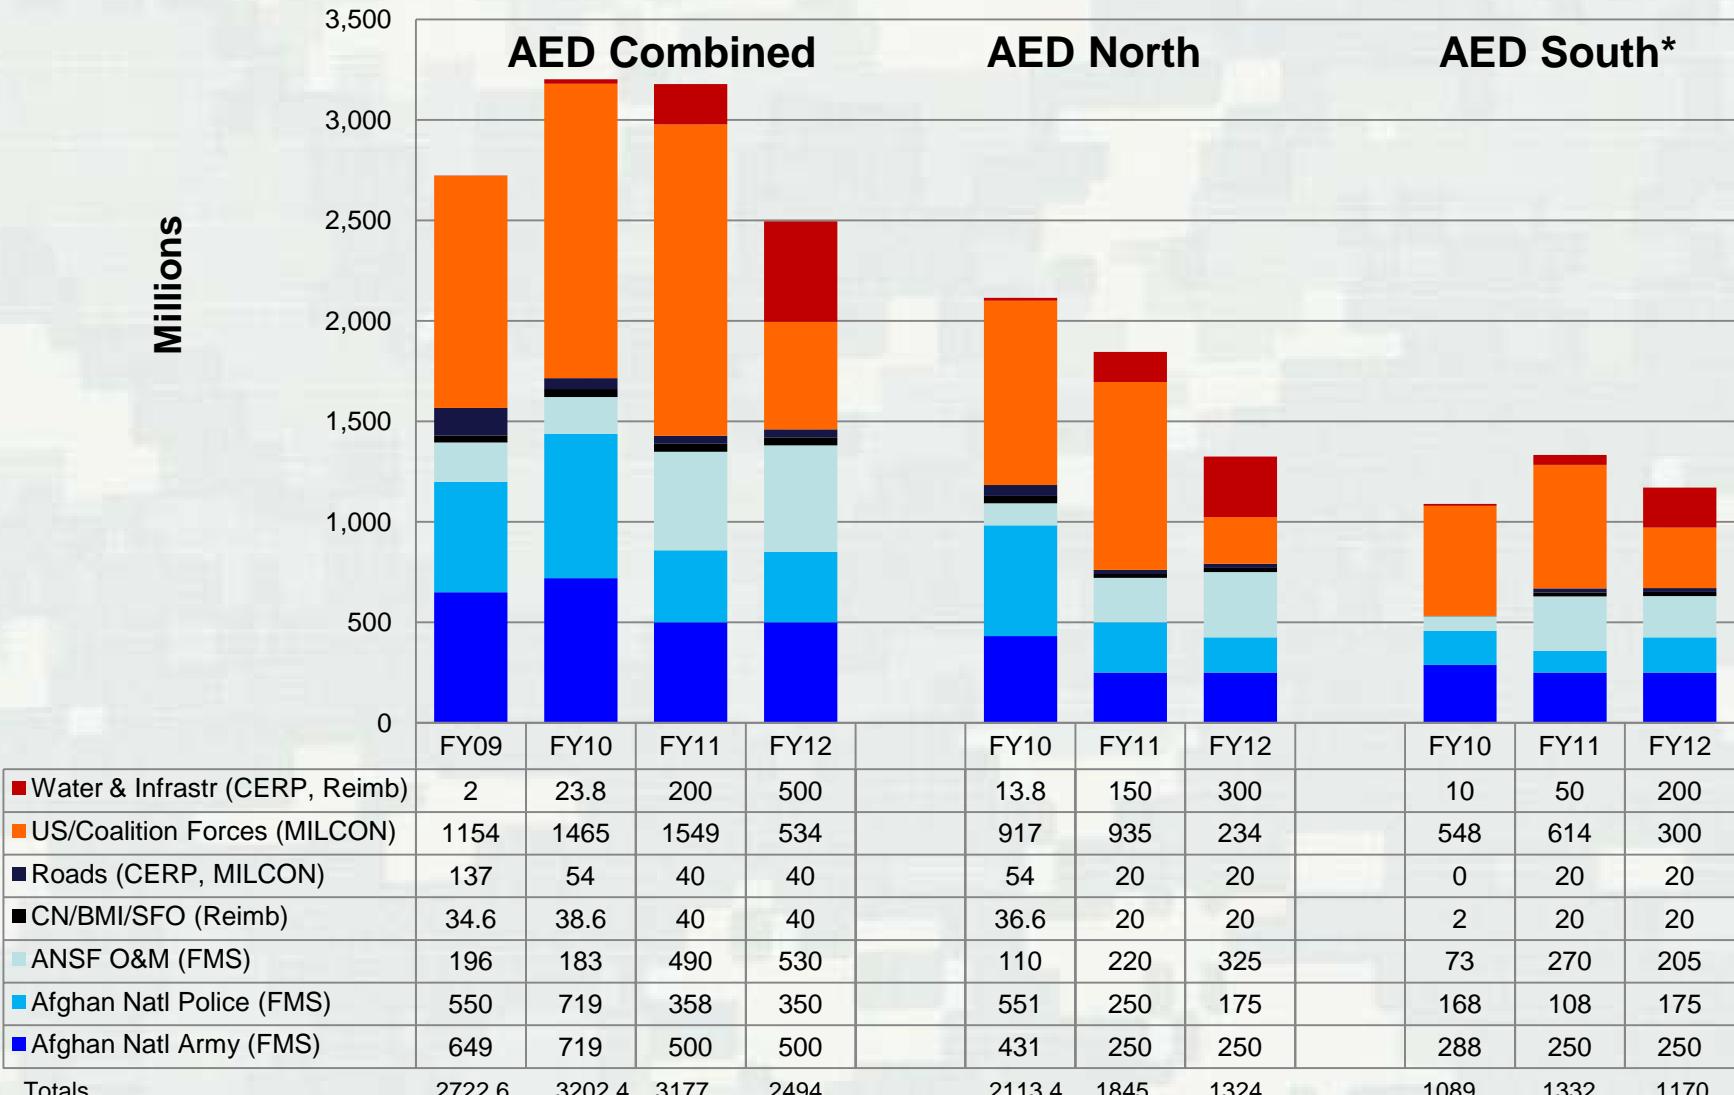

* Note: Does not include AED South work transferred to AFCEE via MOU (work at Bastion)
FY09: \$476M; FY10 \$278M



AED Infrastructure Delivery Initiatives (1 of 2)

- ✓ **Activation of Second District (AES):** Activated AES on 3 Aug 09 to improve engineer support throughout Afghanistan. Improves USACE's capacity to handle the increasing workload. Allows USACE to concentrate resources at critical areas and better integration with Civ / Mil operations in the execution of ANSF and Water & Infrastructure projects.
- ✓ **Align Organization Structure with BSO:** Issued FRAGO defining an Alignment, Movement & Security Plan to align Area Offices with BSOs & PRTs, develop comprehensive QA Assessment plans & leverage security movements to put 'eyes on site' – critical to COIN. Coordinating software to data share project information across CIDNE, RMS, ACSP & Google to leverage QA support and obtain a common operating picture for infrastructure.
- ✓ **PRT Integration / Technical Support:** 40 ea AED sourced civilian engineers / construction reps (2ea / PRT) integrated into US PRTs as technical advisor / QA support. Provide reachback support (to AED and USACE in CONUS) to Maneuver CDRs and USAID for planning and design of technically challenging projects such as the Saracha Bridge replacement, 2PK Power Study, Zama Dam design and the Tom Bridge study.
- ✓ **ANSF Standard Designs:** Developing, awarding standard 'site adapt' designs for ANP facilities (30 Sep09); ANA facilities (15 Jan10) to accelerate contractor mobilization, material procurement and construction – publish design guides for well development, wastewater and geotechnical investigation.
- ✓ **CERP Authority for AED-N / AED-S:** Both Districts will soon have \$200K CERP authority within respective AORs. Must obtain Battlespace owner concurrence prior to construction.



AED Infrastructure Delivery Initiatives (2 of 2)

- ✓ **Enhanced Quality Assurance (QA) Oversight:** Fielding 16 MRAPs, which will integrate with PRTs and Maneuver Convoys to better enable QA oversight of the growing and increasingly dispersed program. Implementing “Aggressive Schedule Management” process to apply contractual remedies early / consistently to mitigate delays and terminations across the theater.
- ✓ **Direct Hire Authority:** Enables fair pay and capacity development by hiring Afghans directly into AED (bypassing current less effective use of personnel services contractor). Request for authority is at OSD-CPP who will request Circular 175 authority from DoS – which will authorize DoD to engage in a bilateral negotiation to amend the exchange of notes and create a labor annex (uncertain timeline for working this through DoS and GIRoA).
- ✓ **Expand “Afghan First” Program:** Establish / create small business-type programs that target geographic areas with project set asides, make sole source procurements, and foster mentor / protégé relationships. Develop minimum wage requirements for all USG construction contracts. Additionally, require formal Afghan subcontracting plans from U.S. and TCN prime contractors.
- ✓ **New Acquisition Tools:** To address growing workload, AED is adding two \$40M JOC (unit price) contracts for countrywide ANSF & US Installation small construction support; two Large MATOCs (\$80M per Task Order); and an AE Rapid Response Services contract to enable agility in support of a dynamic workload.



Upcoming Opportunities – Construction

Project Description:	Magnitude of Construction:	Anticipated RFP Release:
Afghanistan - Sharana, Design/Construct Electrical Distribution Grid	Between \$1,000,000 and \$5,000,000	1 st QTR FY10
Afghanistan - Troop Medical/Dental Clinic, Kandahar	Between \$1,000,000 and \$5,000,000	2 nd QTR FY10
Afghanistan - Perimeter Fence	Between \$1,000,000 and \$5,000,000	3 rd QTR FY10
Iraq- Electrical Grid System	Between \$1,000,000 and \$5,000,000	4 th QTR FY10



Upcoming Opportunities - Services

Project:	Location:	POP/Capacity:	RFP Release:
Afghan National Police O&M	Afghanistan	5yr \$300M	1st Qtr FY10
Afghan National Army O&M	Afghanistan	5yr \$420M	1st Qtr FY10
A/E Services	Afghanistan	5yr \$245M	2nd Qtr FY10
Follow on SCID	Iraq	3yr \$30M	1st Qtr FY10
Follow on CLE	Iraq	3yr \$15M	1st Qtr FY10
Follow on TF SAFE	CENTCOM Wide	2yr \$40M	1st Qtr FY10



Middle East District Contracts

Existing:

- Architect Engineer Indefinite Delivery Contracts
 - Period of Performance through 2014 or until programmatic capacity of \$240M is reached
 - Prime contractors are Baker, Stanley, Tetra Tech, HNTB, Ch2M Hill, Berger

Future:

- Potential Multiple Award Task Order Contracts (MATOC) for Construction
 - Total capacity estimated at \$800M, Potential Award Date of 4th Quarter, FY11



Iraq Contracts

Existing:

- GRC Design Build and General Construction MATOC
 - Period of performance through July 2011 or until programmatic capacity of \$450M is reached
 - Prime contractors are: Aurosta, Almaco Limited, Highland-ICORP, Kufan Group, Futron
- GRC, Camp Cropper General Construction MATOC
 - Period of performance through July 2011 or until programmatic capacity of \$15M is reached
 - Prime contractors are: Piril Construction, Alhamra and Erka
- GRN Design Build and General Construction MATOC
 - Programmatic capacity of \$15M, task orders \$50K - \$5M
 - Prime contractors are: Abilabl, Nanocon, Cosmopolitan, Mercury, Civilian Technologies Limited



Afghanistan Contracts

Future:

- Multiple Award Task Order Contracts (MATOCs) for TAN and TAS
 - Estimated award date Feb 2010
 - Anticipated Capacity of \$240M
 - Up to 5 prime vendors to be selected
- Operations and Maintenance Firm Fixed Price Task Order Contract
 - Estimated award date Feb 2010
 - Anticipated Capacity of \$99M
 - Unit Price Books Used for Pricing



Business Model for Successful Construction in Afghanistan

- Competent and engaged Prime Contractor management
- Actively engaged in leading and mentoring LN and TCN workforce
- Direct participation by prime in day-to-day construction activities
- Investment into internal infrastructure



Capacity Development

- Afghan 1st Program - Increase procurement within Afghanistan of supplies for civilian and military activities
- CASA 1st Program - Encouraged to utilize CASA local sources of supply and service. CASA countries include: Afghanistan, Kazakhstan, Kyrgyzstan, Pakistan, Tajikistan, Turkmenistan, and Uzbekistan
- Clauses – Includes prompt payment within 30 days for all subcontractors, overtime and holiday rate of 1.25, and timely submittal of DBA claims, reports and records
- Local Currency:
 - Iraq: Mandatory use of EFT, payment in local currency
 - Afghanistan: Preferred use of EFT, payment in local currency



FY10 Special Interest and Opportunities

- TAM Industry Day tentatively scheduled for 26 March 2010
 - Will be advertised via FedBizOpps and MED's Public website
- TAM's FY10 Business Opportunities are posted at FedBizOpps
 - www.fbo.gov
- AED's FY10 Business Opportunities are posted at AED's Public website
 - <http://www.aed.usace.army.mil/contracting.asp>
- TAG's opportunities are posted at the Baghdad Business Center
 - <http://www.baghdadbusinesscenter.org/>



Points of Contact

- COL Roemhildt, TAD Deputy Commander (Main), Steven.J.Roemhildt@usace.army.mil
- Colleen O'Keefe, TAD Regional Contracting Chief, Colleen.J.Okeefe@usace.army.mil



P2 Projects Status Report - FY10 & 11 Pending Awards - MED

Report includes all ACTIVE P2 Projects, including "LCM" status (ie, schedules not yet officially built)

Data Date: 7-Mar-2010 / DD + 45 = 21-Apr-2010

Sorted by Installation, Award Date, P2#

Source: OP (Oracle Project)														OP	
#	DIST	INSTL	P2 #	1391	DESCRIPTION	TF	RTA ML180	A S	ADV ML230	A S	OPEN BID ML240	A S	AWARD CC800	A S	P2 Status
1	MED	Afghan	322376	TRKT103100	PM-M, AF - Cargo Handling Area, Tarin Kowt	20-MCAF	17-Apr-09	A	29-Apr-09	A	8-Jul-09	A	15-Mar-10	S	Approved
2	MED	Afghan	330311	072603	AES, 072603, Design/Constr Troop Housing, Ph2, KAF	10-MCA	19-Jan-10	A	19-Jan-10	A	5-Feb-10	A	15-Mar-10	S	Approved
3	MED	Afghan	320516	CMBA093960	PM-M, AF - CAS Apron, Bastion	20-MCAF	17-Jul-09	A	22-Aug-09	A	30-Oct-09	A	20-Mar-10	S	Approved
4	MED	Afghan	320517	CMBA093970	PM-M, AF - Fuels Operations & Storage, Bastion	20-MCAF	17-Jul-09	A	22-Aug-09	A	30-Oct-09	A	20-Mar-10	S	Approved
5	MED	Afghan	322368	ATUH100101	PM-M, Bagram, AF - PAX Terminal	20-MCAF	13-Aug-09	A	29-Sep-09	A	6-Nov-09	A	30-Mar-10	S	Approved
6	MED	Afghan	322370	ATUH103100	PM-M, AF Cargo Terminal-Bagram	20-MCAF	12-Aug-09	A	29-Sep-09	A	6-Nov-09	A	30-Mar-10	S	Approved
7	MED	Afghan	330310	074159	AEN, 074159, Contingency Housing, JAF	10-MCA	8-Dec-09	A	6-Feb-10	A	9-Mar-10	S	31-Mar-10	S	Approved
8	MED	Afghan	330316	074276	AEN, 074276, Troop Housing, Ph3Tombstone/Bastion	10-MCA	11-Sep-09	A	15-Jan-10	A	15-Feb-10	A	12-Apr-10	S	Approved
9	MED	Afghan	330318	074329	AES, 074329, Troop Housing, Ph4, Tombstone/Bastion	10-MCA	11-Sep-09	A	15-Jan-10	A	5-Feb-10	A	12-Apr-10	S	Approved
10	MED	Afghan	330325	074162	AEN, 074162, Contingency Housing, Gardez	10-MCA	8-Dec-09	A	21-Feb-10	S	23-Mar-10	S	13-Apr-10	S	Approved
11	MED	Afghan	320999	073133	AES, 73133, Troop Housing Ph 1, Dwyer	10-MCA	8-Jul-09	A	8-Feb-10	A	19-Mar-10	S	14-Apr-10	S	Approved
12	MED	Afghan	320522	LYAV093300	PM-M, AF - Strat Airlift Apron, Kandahar	20-MCAF	16-Nov-09	A	4-Jan-10	A	23-Feb-10	A	15-Apr-10	S	Approved
13	MED	Afghan	322379	LYAV103200	PM-M, AF Tactical Airlift Apron, Kandahar Air Field	20-MCAF	16-Nov-09	A	4-Jan-10	A	23-Feb-10	A	15-Apr-10	S	Approved
14	MED	Afghan	330309	074102	AEN, 074102, FOB Shank, Design/Constr Troop Housing, Ph2	10-MCA	27-Nov-09	A	27-Nov-09	A	10-Dec-09	A	19-Apr-10	S	Approved
15	MED	Afghan	330591	WACC104220	PM-M - AF, Connecting Taxiway, MeS	20-MCAF	31-Mar-10	S	14-Apr-10	S	30-Apr-10	S	14-May-10	S	Approved
16	MED	Afghan	320445	ATUH093150	PM-M, AF - FY09 CAS Ramp Expansion At Bagram Air Field	20-MCAF	9-Oct-09	A	12-Mar-10	S	1-May-10	S	1-Jul-10	S	Approved
17	MED	Afghan	322548	ATUH103500	PM-M, BAF - Aviation O&M Facilities	20-MCAF	9-Oct-09	A	12-Mar-10	S	1-May-10	S	1-Jul-10	S	Approved
18	MED	Afghan	322549	ATUH103400	PM-M, BAF - Expeditionary Fighter Shelter	20-MCAF	9-Oct-09	A	12-Mar-10	S	1-May-10	S	1-Jul-10	S	Approved
19	MED	Afghan	329160	CMBA103500	PM-M, AF, Cargo Handling Area, Bastion	20-MCAF	22-Jan-10	A	26-Feb-10	A	26-Mar-10	S	2-Jul-10	S	Approved
20	MED	Afghan	329161	CMBA103400	PM-M, AF, Secure RSOI, Bastion	20-MCAF	22-Jan-10	A	26-Feb-10	A	26-Mar-10	S	2-Jul-10	S	Approved
21	MED	Afghan	329162	CMBA103100	PM-M, AF, Strat Airlift Ramp Ext, Bastion	20-MCAF	22-Jan-10	A	26-Feb-10	A	26-Mar-10	S	2-Jul-10	S	Approved
22	MED	Afghan	326085	LYAV103400	PM-M, AF - CAS Apron Expansion, KAF	20-MCAF	8-Mar-10	S	23-Mar-10	S	7-May-10	S	6-Jul-10	S	Approved
23	MED	Afghan	326086	LYAV103500	PM-M, AF - ISR Apron Expansion, Kandahar	20-MCAF	8-Mar-10	S	23-Mar-10	S	7-May-10	S	6-Jul-10	S	Approved
24	MED	Afghan	326087	LYAV103600	PM-M, AF - Aviation O&M Fac, KAF	20-MCAF	8-Mar-10	S	23-Mar-10	S	7-May-10	S	6-Jul-10	S	Approved
25	MED	Afghan	326088	LYAV103700	PM-M, AF - Expeditionary Fighter Shelter, KAF	20-MCAF	8-Mar-10	S	23-Mar-10	S	7-May-10	S	6-Jul-10	S	Approved
26	MED	Afghan	326089	LYAV103800	PM-M, AF - Cargo Helicopter Apron, KAF	20-MCAF	8-Mar-10	S	23-Mar-10	S	7-May-10	S	6-Jul-10	S	Approved
27	MED	Afghan	326096	LYAV103900	PM-M, AF - Relocate North Airfield Road, KAF	20-MCAF	8-Mar-10	S	23-Mar-10	S	7-May-10	S	6-Jul-10	S	Approved
28	MED	Afghan	326098	LYAV103300	PM-M, AF - Refueler Apron/Relocate Hot Cargo Pad, Kandahar	20-MCAF	8-Mar-10	S	23-Mar-10	S	7-May-10	S	6-Jul-10	S	Approved
29	MED	Afghan	329164	CMBA103200	PM-M, AF, CAS Apron Extension, Bastion	20-MCAF	22-Jan-10	A	12-Mar-10	S	12-Apr-10	S	16-Jul-10	S	Approved
30	MED	Afghan	329165	CMBA103300	PM-M, AF, ISR Apron, Bastion	20-MCAF	22-Jan-10	A	12-Mar-10	S	12-Apr-10	S	16-Jul-10	S	Approved
31	MED	Afghan	329167	CMBA103700	PM-M, AF, Expeditionary Fighter Shelter, Bastion	20-MCAF	22-Jan-10	A	12-Mar-10	S	12-Apr-10	S	16-Jul-10	S	Approved
32	MED	Afghan	329169	CMBA103600	PM-M, AF, Aviation Ops & Maintenance Fac, Bastion	20-MCAF	22-Jan-10	A	12-Mar-10	S	12-Apr-10	S	16-Jul-10	S	Approved
33	MED	Afghan	330100	WACC113220	PM-M, AF - Runway, Sharana	20-MCAF	11-May-10	S	24-May-10	S	7-Jul-10	S	31-Aug-10	S	Approved
34	MED	Afghan	330092	WACC104603	PM-M, AF - Fuels Operations & Storage, Shindand	20-MCAF	27-May-10	S	2-Jun-10	S	16-Jul-10	S	5-Sep-10	S	Approved
35	MED	Afghan	330093	WACC104400	PM-M, AF-SOF Heli Apron, Dwyer	20-MCAF	27-May-10	S	2-Jun-10	S	16-Jul-10	S	5-Sep-10	S	Approved
36	MED	Afghan	330095	WACC104600	PM-M, AF-SOF Heli Apron, Shindand	20-MCAF	27-May-10	S	2-Jun-10	S	16-Jul-10	S	5-Sep-10	S	Approved
37	MED	Afghan	330096	WACC104660	PM-M, AF - ISR Apron, Shindand	20-MCAF	27-May-10	S	2-Jun-10	S	16-Jul-10	S	5-Sep-10	S	Approved

P2 Projects Status Report - FY10 & 11 Pending Awards - MED

Report includes all ACTIVE P2 Projects, including "LCM" status (ie, schedules not yet officially built)

Data Date: 7-Mar-2010 / DD + 45 = 21-Apr-2010

Sorted by Installation, Award Date, P2#

Source: OP (Oracle Project)					OP										
#	DIST	INSTL	P2 #	1391	DESCRIPTION	TF	RTA ML180	A S	ADV ML230	A S	OPEN BID ML240	A S	AWARD CC800	A S	P2 Status
38	MED	Afghan	330097	WACC104601	PM-M, AF-SOF ISR Apron & Support Complex, Shindand	20-MCAF	27-May-10	S	2-Jun-10	S	16-Jul-10	S	5-Sep-10	S	Approved
39	MED	Afghan	330103	WACC104602	PM-M, AF, Strategic Airlift Apron, Shindand	20-MCAF	27-May-10	S	2-Jun-10	S	16-Jul-10	S	5-Sep-10	S	Approved
40	MED	Afghan	330104	WACC104650	PM-M, AF-Munitions Storage Area, Shindand	20-MCAF	27-May-10	S	2-Jun-10	S	16-Jul-10	S	5-Sep-10	S	Approved
41	MED	Afghan	330593	WACC114550	PM-M - AF, Passenger and Cargo Terminal, Shindand	20-MCAF	27-May-10	S	2-Jun-10	S	16-Jul-10	S	5-Sep-10	S	Approved
42	MED	Afghan	330861		PM-M, AF, Runway Repair, Kunduz	24-OMAF	27-May-10	S	02-Jun-10	S	16-Jul-10	S	05-Sep-10	S	LCM
43	MED	Afghan	330091	WACC104300	PM-M, AF - Apron, Delaram	20-MCAF	15-May-10	S	30-May-10	S	15-Jul-10	S	15-Sep-10	S	Approved
44	MED	Afghan	330094	WACC104210	PM-M, AF - Helicopter Apron, Mazar E Sharif	20-MCAF	29-May-10	S	30-May-10	S	15-Jul-10	S	15-Sep-10	S	Approved
45	MED	Afghan	330101	WACC104200	PM-M, AF, Strategic Airlift Apron, Mazar E Sharif	20-MCAF	29-May-10	S	30-May-10	S	15-Jul-10	S	15-Sep-10	S	Approved
46	MED	Afghan	330105	WACC104310	PM-M, AF-Runway, Delaram	20-MCAF	15-May-10	S	30-May-10	S	15-Jul-10	S	15-Sep-10	S	Approved
47	MED	Afghan	330324	072605	AEN, 072605, Troop Housing PH 3, BAF	10-MCA	19-Feb-10	S	21-Jul-10	S	4-Sep-10	S	30-Sep-10	S	Approved
48	MED	Afghan	330018	KARD113200	PM-M, AF, Expeditionary Airlift Shelter, Kandahar	20-MCAF	8-Oct-10	S	14-Oct-10	S	27-Nov-10	S	26-Jan-11	S	Approved
49	MED	Afghan	330019	KARD113100	PM-M, AF, Expand Cargo Handling Area, Kandahar	20-MCAF	8-Oct-10	S	14-Oct-10	S	27-Nov-10	S	26-Jan-11	S	Approved
50	MED	Afghan	329985	ATUH110101	PM-M, AF - Construct Consolidated Rigging Facility, Bagram	20-MCAF	12-Aug-10	S	28-Aug-10	S	12-Oct-10	S	1-Feb-11	S	Approved
51	MED	Afghan	330011	ATUH110103	PM-M, AF - MEDEVAC Ramp Exp & Fire Station, Bagram	20-MCAF	12-Aug-10	S	28-Aug-10	S	12-Oct-10	S	1-Feb-11	S	Approved
52	MED	Afghan	330017	ATUH110104	PM-M, AF - Fighter Hanger, Bagram	20-MCAF	12-Aug-10	S	28-Aug-10	S	12-Oct-10	S	1-Feb-11	S	Approved
53	MED	Afghan	330862	CMBA113400	PM-M, AF, Expand Fuel Ops & Storage, Bastion	20-MCAF	10-Oct-10	S	15-Oct-10	S	15-Dec-10	S	15-Mar-11	S	Approved
54	MED	Afghan	330863	CMBA113200	PM-M, AF, Refueler Apron, Bastion	20-MCAF	10-Oct-10	S	15-Oct-10	S	15-Dec-10	S	15-Mar-11	S	Approved
55	MED	Afghan	330868		PM-M, AF, Parallel Taxiway, Bastion	20-MCAF	10-Oct-10	S	15-Oct-10	S	15-Dec-10	S	15-Mar-11	S	Approved
56	MED	Bahrain	115816	P-926	PM-M, BA - P-926 SOF Operations Facility	4S-SOF	3-Apr-08	A	27-May-08	A	28-Jun-08	A	15-Apr-10	S	Approved
57	MED	Bahrain	140298	P928	PM-M, BA - P-928 Waterfront Dev PHII	30-MCN	30-Mar-10	S	30-Mar-10	S	17-May-10	S	19-Jul-10	S	Approved
58	MED	Bahrain	329156	VKWD113100	PM-M, BH, North Apron Expansion - Isa Air Base	20-MCAF	4-Oct-10	S	5-Oct-10	S	18-Nov-10	S	26-Jan-11	S	Approved
59	MED	Bahrain	327444	P908	PM-M, P908 Operations & Support Facilities	30-MCN	14-Feb-11	S	15-Feb-11	S	31-Mar-11	S	16-May-11	S	Approved
60	MED	Bahrain	327442		PM-M - BA, P954 Waterfront Development Phase 3	30-MCN	22-Jun-11	S	23-Jun-11	S	6-Aug-11	S	21-Sep-11	S	Approved
61	MED	Egypt	115894		PM-F, EG - EGYPT TRANS DEPT EQUIPMENT	70-FMS	17-Feb-10	A	17-Feb-10	A	17-Feb-10	A	15-Mar-10	S	Approved
62	MED	Egypt	321020		PM-F E6-B-HCC, Rock Crush/Screen Plant	70-FMS	7-Jan-10	A	7-Jan-10	A	21-Jan-10	A	15-Mar-10	S	Approved
63	MED	Egypt	115868		PM-F, EG - SYNCROLIFTS O&M	70-FMS	16-Mar-10	S	16-Mar-10	S	16-Mar-10	S	17-Mar-10	S	Approved
64	MED	Egypt	326599		PM-F, EG, HCO Procure Bulldozers	70-FMS	17-Dec-09	A	17-Dec-09	A	16-Feb-10	A	31-Mar-10	S	Approved
65	MED	Egypt	325106		PM-F, Egypt - HCM/UPG IM Equip Procure/Deliver/Inspect	70-FMS	15-Mar-10	S	15-Mar-10	S	4-Apr-10	S	19-Apr-10	S	Approved
66	MED	Egypt	321579		PM-F, EG HCG Multi-purpose Loaders (40 ea)	70-FMS	18-Dec-09	A	18-Dec-09	A	13-Apr-10	S	28-Apr-10	S	Approved
67	MED	Egypt	321519		PM-F, EG - HCK Water Well Drilling System	70-FMS	15-Mar-10	S	15-Mar-10	S	15-Apr-10	S	4-May-10	S	Approved
68	MED	Egypt	132001		PM-F, EG - Medical Equip for EAF (EG-B-HBP)	70-FMS	8-Apr-10	S	8-Apr-10	S	22-Apr-10	S	7-May-10	S	Approved
69	MED	Egypt	327080		PM-F, EGBHCP, Procurement of Engr Equip Ph III	70-FMS	27-Mar-10	S	28-Mar-10	S	26-Apr-10	S	11-May-10	S	Approved
70	MED	Egypt	322367		PM-F, EG - HCJ Automated Concrete Plant	70-FMS	30-Mar-10	S	30-Mar-10	S	27-Apr-10	S	14-May-10	S	Approved
71	MED	Egypt	321016		PM-F, E6-B-HCB, Procure Case Asphalt Equip	70-FMS	18-Mar-10	S	18-Mar-10	S	16-Apr-10	S	16-May-10	S	Approved
72	MED	Egypt	331073		PM-F, EG, HCR, Procure TRNG-HW-SW, MMC Computer Tech Suppor	70-FMS	01-Jun-10	S	01-Jun-10	S	21-Jun-10	S	21-Jul-10	S	LCM
73	MED	Egypt	324065		PM-F, EG - HCH Construction Equipment Services	70-FMS	2-Jul-10	S	2-Jul-10	S	17-Jul-10	S	1-Aug-10	S	Approved
74	MED	Egypt	329786		PM-F, EG, Construct Base Facilities VBT	70-FMS	22-Apr-10	S	06-May-10	S	12-Jul-10	S	16-Sep-10	S	LCM

P2 Projects Status Report - FY10 & 11 Pending Awards - MED

Report includes all ACTIVE P2 Projects, including "LCM" status (ie, schedules not yet officially built)

Data Date: 7-Mar-2010 / DD + 45 = 21-Apr-2010

Sorted by Installation, Award Date, P2#

Source: OP (Oracle Project)																OP
#	DIST	INSTL	P2 #	1391	DESCRIPTION	TF	RTA ML180	A S	ADV ML230	A S	OPEN BID ML240	A S	AWARD CC800	A S	P2 Status	
75	MED	Jordan	326440		PM-F, JO Constr Madaba Medical Clinic	WX-SOOTH	1-Mar-10	S	16-Mar-10	S	15-Apr-10	S	17-May-10	S	Approved	
76	MED	Jordan	326215		PM-F, JO Constr Shuna Med Clinic	WX-SOOTH	1-Mar-10	S	31-Mar-10	S	30-Apr-10	S	1-Jun-10	S	Approved	
77	MED	Jordan	155892		PM-F, JO - Design Development C4ISR	70-FMS	25-Jun-10	S	30-Jun-10	S	30-Jul-10	S	20-Aug-10	S	Approved	
78	MED	Jordan	326547		PM-F, ERC Jordan, Vehicle Maint., Slab for DFAC, Latrine Pad	33-OMN	16-Jul-10	S	19-Jul-10	S	30-Aug-10	S	20-Oct-10	S	Approved	
79	MED	Kuwait	321886	071485	PM-M, KU, APS - 5 Stocks	10-MCA	2-Nov-09	A	17-Jun-10	S	2-Aug-10	S	30-Aug-10	S	Approved	
80	MED	Kyrgyzstan	150969	BRVN090100	PM-M, KY - Remote Parking Area at Manas Transit Center, Kyrgyzstan	20-MCAF	22-Dec-09	A	23-Dec-09	A	16-Feb-10	A	15-Mar-10	S	Approved	
81	MED	Lebanon	326202		PM-F, LB - Repair Sin El-Fil Public School	WX-SOOTH	1-Mar-10	S	16-Mar-10	S	16-Apr-10	S	17-May-10	S	Approved	
82	MED	Lebanon	326358		PM-F, LB - Repair Haret Sakhr Public School	WX-SOOTH	1-Mar-10	S	17-Mar-10	S	16-Apr-10	S	17-May-10	S	Approved	
83	MED	Lebanon	326363		PM-F, LB Repair Almat Public School	WX-SOOTH	1-Mar-10	S	17-Mar-10	S	16-Apr-10	S	17-May-10	S	Approved	
84	MED	Lebanon	326364		PM-F, LB Const Sanitary Sewer Dist Sys	WX-SOOTH	2-Mar-10	S	17-Mar-10	S	19-Apr-10	S	19-May-10	S	Approved	
85	MED	Lebanon	326367		PM-F, LB Const Badero X-Ray Annex	WX-SOOTH	1-Mar-10	S	26-Mar-10	S	27-Apr-10	S	26-May-10	S	Approved	
86	MED	Oman	330424		PM-M, OM, Repair Airfield 17-35	24-OMAF	1-Jul-10	S	1-Jul-10	S	4-Aug-10	S	21-Sep-10	S	Approved	
87	MED	Oman	330425		PM-M, OM, Repair Airfield 17-35	24-OMAF	2-Jul-10	S	2-Jul-10	S	3-Aug-10	S	22-Sep-10	S	Approved	
88	MED	Pakistan	329095		PM-F, PK, Design/Construct Border Coordination Center, Chitral, Paki	Z2-DODO	4-May-10	S	4-Jun-10	S	6-Jul-10	S	4-Aug-10	S	Approved	
89	MED	Qatar	132587	ALDA053001A	PM-M, QA - Multi Aircraft Maintenance Hangar, Al Udeid Airbase	20-MCAF	11-Jun-08	A	16-Dec-08	A	10-Feb-09	A	15-Mar-10	S	Approved	
90	MED	Qatar	154908	ALUA073008A	PM-M, QA - Facilities Replacement AUAB	20-MCAF	22-Dec-08	A	22-Dec-08	A	10-Feb-09	A	15-Mar-10	S	Approved	
91	MED	Qatar	149794	ALUA073004	PM-M, QA - Construct CAS Ramp Al Udeid	20-MCAF	22-May-09	A	22-May-09	A	18-Aug-09	A	22-Mar-10	S	Approved	
92	MED	Qatar	326549	ALUA080126	PM-M, QA, Relocate South MSA	20-MCAF	17-Feb-10	A	19-Feb-10	A	8-Apr-10	S	14-May-10	S	Approved	
93	MED	Qatar	320779	ALUA073006A	PM-M, QA - FY10 Blatchford Preston Complex Phase 2	20-MCAF	19-Mar-10	S	22-Mar-10	S	30-Apr-10	S	30-Jul-10	S	Approved	
94	MED	Qatar	324458		PM-M, QA Force Protection Measures, ECP, Gate #2	23-MMAF	28-Apr-10	S	28-Apr-10	S	28-May-10	S	30-Jul-10	S	Approved	
95	MED	Qatar	330905		PM-M, QA, FFE for Logistics Storage Warehouse, Qatar	14-OMA	30-Apr-10	S	3-Jun-10	S	28-Jun-10	S	31-Aug-10	S	Approved	
96	MED	Qatar	328477	ALUA073006B	PM-M, QA - BPC Phase 3	20-MCAF	19-Aug-10	S	23-Aug-10	S	6-Oct-10	S	20-Jan-11	S	Approved	
97	MED	Qatar	328358	ALDA070198	PM-M, QA - Defense Logistics Warehouse, ALUD, Qatar	Z2-DODO	20-Sep-10	S	28-Sep-10	S	29-Nov-10	S	2-Feb-11	S	Approved	
98	MED	Saudi	115842		PM-F, Saudi HEG Case GDMW Computer Services	70-FMS	31-Mar-10	S	31-Mar-10	S	14-Apr-10	S	29-Apr-10	S	Approved	
99	MED	Saudi	326744		PM-M - SA, Design Four Southgate Projects at Eskan Village	24-OMAF	24-Mar-10	S	14-Apr-10	S	17-Jun-10	S	20-Aug-10	S	Approved	
100	MED	Tajikistan	330983		PM-F, TJ, D-B Tajik National Training Center	14-OMA	3-May-10	S	4-May-10	S	4-May-10	S	4-May-10	S	Approved	
101	MED	UAE	145268		PM-F, UAE - Blackhawk/Apron O&M Utilities	70-FMS	17-Aug-09	A	3-Jan-10	A	9-Mar-10	S	16-Mar-10	S	Approved	
102	MED	Yemen	145194		PM-F, YE - Constr Floating Pier#1 Khar Mayrat	70-FMS	20-Aug-09	A	20-Aug-09	A	13-Nov-09	A	1-Apr-10	S	Approved	

P2 Projects Status Report - FY10 & 11 Pending Awards - AED

Report includes all ACTIVE P2 Projects, including "LCM" status (ie, schedules not yet officially built)

Data Date: 7-Mar-2010 / DD + 45 = 21-Apr-2010

Sorted by Award Date, P2#

Source: OP (Oracle Project)														OP	
#	DIST	INSTL	P2 #	1391	DESCRIPTION	TF	RTA ML180	A S	ADV ML230	A S	OPEN BID ML240	A S	AWARD CC800	A S	P2 Status
1	AED	Afghan	323749	071491	AEN, 071491, APS Compound, BAF	10-MCA	4-Nov-09	A	4-Nov-09	A	3-Dec-09	A	12-Mar-10	S	Approved
2	AED	Afghan	321007	073408	AES, 073408 Fuel Distribution System, Dwyer	10-MCA	15-Dec-09	A	15-Dec-09	A	21-Jan-10	A	15-Mar-10	S	Approved
3	AES	Afghan	326354	074147	AES, 074147, Fuel System Ph 1, Dwyer	10-MCA	15-Dec-09	A	1-Jan-10	A	29-Jan-10	A	15-Mar-10	S	Approved
4	AED	Afghan	320695	073209	AES, 073209 AV Hangar/Maint Facs, Bastion	10-MCA	22-Aug-09	A	3-Nov-09	A	17-Nov-09	A	17-Mar-10	S	Approved
5	AED	Afghan	323173	069398	AEN - 069398, Bulk Fuel Storage/Supply Ph 6, IBAF	10-MCA	17-Dec-09	A	18-Dec-09	A	27-Jan-10	A	18-Mar-10	S	Approved
6	AED	Afghan	323176	069403	AEN - 069403, Bulk Fuel Storage/Supply Ph 7, IBAF	10-MCA	17-Dec-09	A	18-Dec-09	A	27-Jan-10	A	18-Mar-10	S	Approved
7	AED	Afghan	321001	073129	AES, 73129, Troop Housing Ph2, Tombstone	10-MCA	31-Jul-09	A	15-Jan-10	A	5-Feb-10	A	20-Mar-10	S	Approved
8	AEN	Afghan	326334	074172	AEN - 074172, Camp Phoenix Western Expansion, Kabul	10-MCA	16-Feb-10	S	17-Feb-10	S	17-Feb-10	S	22-Mar-10	S	Approved
9	AED	Afghan	320519	073207	AES, 073207 Rotary Wing Ramp and Taxiways PH 2, Bastion	10-MCA	14-Aug-09	A	3-Nov-09	A	17-Nov-09	A	24-Mar-10	S	Approved
10	AED	Afghan	320858	073239	AEN, 073239 Aviation Hangar Maintenance Facility, Shank	10-MCA	24-Sep-09	A	26-Sep-09	A	29-Oct-09	A	24-Mar-10	S	Approved
11	AED	Afghan	320859	073364	AED, Rotary Wing Park & Taxiway Ph 2, Shank	10-MCA	24-Sep-09	A	26-Sep-09	A	29-Oct-09	A	24-Mar-10	S	Approved
12	AES	Afghan	330312	073195	AES, 073195, FOB, Contingency Housing, Dwyer	10-MCA	8-Feb-10	A	8-Feb-10	A	24-Feb-10	S	24-Mar-10	S	Approved
13	AES	Afghan	330315	074330	AES, 074330, Contingency Housing, Ph 2, Dwyer	10-MCA	8-Feb-10	A	8-Feb-10	A	24-Feb-10	S	24-Mar-10	S	Approved
14	AES	Afghan	330317	074326	AEN, 074326, Contingency Housing, Ph 1, Dwyer	10-MCA	7-Feb-10	A	8-Feb-10	A	24-Feb-10	S	24-Mar-10	S	Approved
15	AED	Afghan	321004	073230	AEN, 73230, Troop Housing Ph 1, Airborne Wardak	10-MCA	1-Aug-09	A	24-Nov-09	A	23-Feb-10	S	31-Mar-10	S	Approved
16	AED	Afghan	321075	073236	AEN, 73236, Temp Housing Ph 1 - Altimur	10-MCA	19-Jul-09	A	24-Nov-09	A	20-Dec-09	A	31-Mar-10	S	Approved
17	AEN	Afghan	324943	SHNK103100	AED, SHNK103100, Cargo Handling Area, Shank	20-MCAF	18-Feb-10	A	18-Feb-10	S	11-Mar-10	S	31-Mar-10	S	Approved
18	AES	Afghan	326299	074143	AES, 074143, Entry Control Point & Access Roads, Tombstonstone/B	10-MCA	15-Dec-09	A	15-Dec-09	A	3-Feb-10	A	13-Apr-10	S	Approved
19	AES	Afghan	326368	073100	AES, 073100, Basic Load Ammunition Holding Area, Tombstone	10-MCA	15-Dec-09	A	15-Dec-09	A	3-Feb-10	A	13-Apr-10	S	Approved
20	AED	Afghan	321003	073233	AEN, 073233, Troop Housing Ph 1, Shank	10-MCA	28-Jul-09	A	27-Nov-09	A	10-Dec-09	A	19-Apr-10	S	Approved
21	AEN	Afghan	326278	074103	AEN, 074103, Waste Management Complex, Shank	10-MCA	22-Mar-10	S	22-Mar-10	S	11-Apr-10	S	26-Apr-10	S	Approved
22	AEN	Afghan	326279	074195	AEN, 074195, Water Distribution System, Shank	10-MCA	22-Mar-10	S	22-Mar-10	S	11-Apr-10	S	26-Apr-10	S	Approved
23	AES	Afghan	326349	074181	AES, 074181, Waste Management Area, Tarin Kwo	10-MCA	14-Mar-10	S	15-Mar-10	S	29-Mar-10	S	29-Apr-10	S	Approved
24	AES	Afghan	326294	074319	AES, 074319, Water Supply & Distribution System, Tombstonstone/B	10-MCA	20-Jan-10	A	20-Jan-10	A	18-Feb-10	A	30-Apr-10	S	Approved
25	AES	Afghan	326295	074274	AES, 074274, Roads, Tombstone/Bastion	10-MCA	20-Jan-10	A	20-Jan-10	A	18-Feb-10	A	30-Apr-10	S	Approved
26	AED	Afghan	321043	073389	AEN, 73389, Troop Housing (2130 PAX) - BAF	10-MCA	26-Jun-10	S	1-Mar-10	S	6-Apr-10	S	6-May-10	S	Approved
27	AES	Afghan	326313	074203	AES, 074203, Waste Management Area, Maywand	10-MCA	14-Mar-10	S	15-Mar-10	S	7-Apr-10	S	6-May-10	S	Approved
28	AES	Afghan	326351	074169	AES, 074169, Waste Management Area, Wolverine	10-MCA	14-Mar-10	S	15-Mar-10	S	7-Apr-10	S	6-May-10	S	Approved
29	AED	Afghan	321006	073407	AES, 073407 Distribution System, Bastion	10-MCA	2-Mar-10	S	2-Mar-10	S	5-Apr-10	S	8-May-10	S	Approved
30	AED	Afghan	321078	073126	AES, 073126 Temp Housing Ph 1, Tombstone	10-MCA	31-Jul-09	A	15-Jan-10	A	5-Feb-10	A	9-May-10	S	Approved
31	AED	Afghan	321005	073409	AES, 073409 Fuel Distribution System, Tarin Kwo	10-MCA	1-Apr-10	S	2-Apr-10	S	2-Apr-10	S	11-May-10	S	Approved
32	AES	Afghan	326331	074145	AES, 074145, Fuel System Ph 2, Tarin Kwo	10-MCA	19-Mar-10	S	22-Mar-10	S	28-Mar-10	S	11-May-10	S	Approved
33	AEN	Afghan	326282	074117	AEN, 074117, Waste Management Area, Salerno	10-MCA	8-Apr-10	S	9-Apr-10	S	29-Apr-10	S	20-May-10	S	Approved
34	AEN	Afghan	326283	074120	AEN, 074120, Waste Management Area, Ghazni	10-MCA	8-Apr-10	S	9-Apr-10	S	29-Apr-10	S	20-May-10	S	Approved
35	AES	Afghan	330550	076963	AES, 076963, Fire Station, Tarin Kwo	10-MCA	14-Apr-10	S	14-Apr-10	S	5-May-10	S	20-May-10	S	Approved
36	AES	Afghan	330551	076965	AES, 076965, Fire Station, Maywand	10-MCA	14-Apr-10	S	14-Apr-10	S	5-May-10	S	20-May-10	S	Approved
37	AES	Afghan	330559	076964	AES, 076964, Fire Station, Spin Boldak	10-MCA	14-Apr-10	S	14-Apr-10	S	5-May-10	S	20-May-10	S	Approved

P2 Projects Status Report - FY10 & 11 Pending Awards - AED

Report includes all ACTIVE P2 Projects, including "LCM" status (ie, schedules not yet officially built)

Data Date: 7-Mar-2010 / DD + 45 = 21-Apr-2010

Sorted by Award Date, P2#

Source: OP (Oracle Project)																	OP
#	DIST	INSTL	P2 #	1391	DESCRIPTION	TF	RTA ML180	A S	ADV ML230	A S	OPEN BID ML240	A S	AWARD CC800	A S	P2 Status		
38	AES	Afghan	326286	074171	AES, 074171, Waste Management Area, Dwyer	10-MCA	9-Mar-10	S	12-Apr-10	S	12-May-10	S	26-May-10	S	Approved		
39	AED	Afghan	324543	071489	AEN, 071489, Barracks, Ph 11-14, BAF	10-MCA	12-Mar-10	S	13-Mar-10	S	11-Apr-10	S	7-Jun-10	S	Approved		
40	AEN	Afghan	327095	074134	AED - 074134, BAF Construct Access Roads	10-MCA	4-Apr-10	S	5-Apr-10	S	25-Mar-10	S	8-Jun-10	S	Approved		
41	AES	Afghan	326271	074149	AES, 074149, Waste Management Complex, KAF	10-MCA	7-Mar-10	S	1-Apr-10	S	17-May-10	S	10-Jun-10	S	Approved		
42	AES	Afghan	326261	073099	AES - 073099, Command & Control Facility, KAF	10-MCA	14-Mar-10	S	15-Mar-10	S	29-Apr-10	S	14-Jun-10	S	Approved		
43	AES	Afghan	326263	073097	AES - 073097, Command & Control Facility, KAF	10-MCA	14-Mar-10	S	15-Mar-10	S	29-Apr-10	S	14-Jun-10	S	Approved		
44	AES	Afghan	326264	073082	AES - 073082, Command & Control Facility, KAF	10-MCA	14-Mar-10	S	15-Mar-10	S	29-Apr-10	S	14-Jun-10	S	Approved		
45	AED	Afghan	320848	073223	AES, 73223, Medical Facility- Dwyer	10-MCA	3-Apr-10	S	4-Apr-10	S	3-May-10	S	17-Jun-10	S	Approved		
46	AED	Afghan	320943	073212	AES, 73212, Troop Medical/Dental Clinic, Kandahar	10-MCA	24-Jul-10	S	24-Jul-10	S	25-Jul-10	S	17-Jun-10	S	Approved		
47	AED	Afghan	321044	072243	AEN, 072243 Construct Drainage Improvements, BAF	10-MCA	30-Mar-10	S	31-Mar-10	S	14-May-10	S	29-Jun-10	S	Approved		
48	AEN	Afghan	325736	073124	AEN, 073124, Drainage System Ph 2, BAF	10-MCA	30-Mar-10	S	31-Mar-10	S	14-May-10	S	29-Jun-10	S	Approved		
49	AES	Afghan	326352	ACC103910	AES, ACC103910, Cargo Handling Area, Dwyer-Garmsir	20-MCAF	24-Feb-10	S	3-Mar-10	S	17-Apr-10	S	29-Jun-10	S	Approved		
50	AEN	Afghan	329522	077243	AEN, 077243, Rotary Wing Parking, Airborne	10-MCA	24-Mar-10	S	30-Apr-10	S	30-May-10	S	29-Jun-10	S	Approved		
51	AEN	Afghan	329595	077242	AEN, 077242, Rotary Wing Parking, Jalalabad	10-MCA	26-Mar-10	S	30-Apr-10	S	30-May-10	S	29-Jun-10	S	Approved		
52	AES	Afghan	326272	073106	AES, 073106, South Park Roads, KAF	10-MCA	30-Apr-10	S	30-Apr-10	S	30-May-10	S	30-Jun-10	S	Approved		
53	AES	Afghan	326265	074296	AES, 074296, Theater Vehicle Maintenance Compound, KAF	10-MCA	21-Apr-10	S	22-Apr-10	S	21-May-10	S	2-Jul-10	S	Approved		
54	AED	Afghan	322543	072126	AEN 072126, Command and Control Facility, BAF	10-MCA	13-Apr-10	S	13-Apr-10	S	27-May-10	S	19-Jul-10	S	Approved		
55	AED	Afghan	320856	073232	AEN, 73232, Rotary/Wing Ramp & Taxiway PH 1, Sharana	10-MCA	27-Apr-10	S	27-Apr-10	S	11-Jun-10	S	26-Jul-10	S	Approved		
56	AED	Afghan	320860	073080	AEN, 073080, Aviation Maintenance Facility, Sharana	10-MCA	27-Apr-10	S	27-Apr-10	S	11-Jun-10	S	26-Jul-10	S	Approved		
57	AED	Afghan	320861	073367	AEN, 73367, Rotary/Wing Park/Taxi Ph 2 Sharana	10-MCA	27-Apr-10	S	27-Apr-10	S	11-Jun-10	S	26-Jul-10	S	Approved		
58	AEN	Afghan	326338	074206	AEN, 074206, Rotary-Wing Parking, Sharana	10-MCA	26-Apr-10	S	27-Apr-10	S	11-Jun-10	S	26-Jul-10	S	Approved		
59	AEN	Afghan	326359	074234	AEN, 074234, Fuel System Ph 1, Salerno	10-MCA	8-Jun-10	S	8-Jun-10	S	7-Jul-10	S	26-Jul-10	S	Approved		
60	AES	Afghan	326269	074292	AES, 074292, Warehouse, KAF	10-MCA	26-May-10	S	5-Jul-10	S	19-Jul-10	S	6-Aug-10	S	Approved		
61	AEN	Afghan	326339	074207	AEN, 074207, Ammunition Supply Point, Sharana	10-MCA	16-Jun-10	S	18-Jun-10	S	18-Jul-10	S	6-Aug-10	S	Approved		
62	AES	Afghan	329589	075203	AES, 075203, Rotary Wing Apron Ph2, Dwyer	10-MCA	6-Apr-10	S	30-May-10	S	15-Jul-10	S	15-Aug-10	S	Approved		
63	AES	Afghan	326353	074146	AES, 074146, Fuel System Ph 1, Wolverine	10-MCA	29-Jun-10	S	1-Jul-10	S	30-Jul-10	S	19-Aug-10	S	Approved		
64	AEN	Afghan	326229	074154	AEN, 074154, Medlog Warehouse, BAF	10-MCA	26-May-10	S	27-May-10	S	8-Jul-10	S	24-Aug-10	S	Approved		
65	AEN	Afghan	326306	074136	AEN, 074136, Command & Control Facility, BAF	10-MCA	27-May-10	S	27-May-10	S	8-Jul-10	S	24-Aug-10	S	Approved		
66	AES	Afghan	329424	075210	AES, 075210, Expand Utilities Ph 2, KAF	EA-MCCA	26-May-10	S	31-May-10	S	15-Jul-10	S	26-Aug-10	S	Approved		
67	AEN	Afghan	326305	074285	AEN - 074285, Runway Upgrade, Salerno	10-MCA	26-May-10	S	28-May-10	S	13-Jul-10	S	27-Aug-10	S	Approved		
68	AED	Afghan	323748	073208	AES, 073208 - , Role 2 Med Fac, Tombstone	10-MCA	28-Jun-10	S	28-Jun-10	S	4-Aug-10	S	20-Sep-10	S	Approved		
69	AEN	Afghan	325449	074221	AEN, 074221, Perimeter Fence, Jalalabad	10-MCA	25-Jun-10	S	25-Jun-10	S	25-Jul-10	S	28-Sep-10	S	Approved		
70	AEN	Afghan	326342	074219	AEN - 074219, Ammunition Supply Point, Jalalabad	10-MCA	25-Jun-10	S	6-Jul-10	S	9-Aug-10	S	28-Sep-10	S	Approved		
71	AES	Afghan	329260	076292	AES, 076292 Rotary-Wing Ramp & Taxiway, Shindand	EA-MCCA	10-May-10	S	25-May-10	S	11-Jul-10	S	29-Sep-10	S	LCM		
72	AES	Afghan	329284	076293	AES, 076293 Rotary-Wing Ramp & Taxiway, Herat	10-MCA	10-May-10	S	25-May-10	S	11-Jul-10	S	29-Sep-10	S	LCM		
73	AES	Afghan	329286	076145	AED, AF, 076145 Waste Mgmt Complex, Shindand	23-MMAF	10-May-10	S	25-May-10	S	11-Jul-10	S	29-Sep-10	S	LCM		
74	AES	Afghan	329287	076288	AES, 076288 Waste Mgmt Complex, Herat	10-MCA	10-May-10	S	25-May-10	S	11-Jul-10	S	29-Sep-10	S	LCM		

P2 Projects Status Report - FY10 & 11 Pending Awards - AED

Report includes all ACTIVE P2 Projects, including "LCM" status (ie, schedules not yet officially built)

Data Date: 7-Mar-2010 / DD + 45 = 21-Apr-2010

Sorted by Award Date, P2#

Source: OP (Oracle Project)																	OP
#	DIST	INSTL	P2 #	1391	DESCRIPTION	TF	RTA ML180	A S	ADV ML230	A S	OPEN BID ML240	A S	AWARD CC800	A S	P2 Status		
75	AES	Afghan	329288	076290	AES, 076290 Construct Tactical Runway, Shindand	10-MCA	10-May-10	S	25-May-10	S	11-Jul-10	S	29-Sep-10	S	LCM		
76	AES	Afghan	329289	076289	AES, 076289 Waste Mgmt Complex, Farah	10-MCA	10-May-10	S	25-May-10	S	11-Jul-10	S	29-Sep-10	S	LCM		
77	AED	Afghan	322540	071493	AEN, 071493 - AF, Perimeter Fence/Guard Towers, BAF	10-MCA	28-Mar-10	S	15-Jul-10	S	14-Aug-10	S	23-Oct-10	S	Approved		
78	AEN	Afghan	327449	069404	AEN, 069404, Joint Defense Operations Center, BAF	10-MCA	20-Jun-10	S	27-Jul-10	S	14-Sep-10	S	29-Oct-10	S	Approved		
79	AEN	Afghan	329640	075080	AEN, 075085, Guard Towers, Shank	10-MCA	8-May-10	S	27-Jul-10	S	14-Sep-10	S	29-Oct-10	S	Approved		
80	AEN	Afghan	329641	074462	AEN, 074462, Bulk Materials Transfer Station, Sharana	10-MCA	4-Jul-10	S	27-Jul-10	S	14-Sep-10	S	29-Oct-10	S	Approved		
81	AEN	Afghan	329530	074104	AEN, 074104, Theater Support Fac, BAF	10-MCA	1-Aug-10	S	1-Aug-10	S	15-Sep-10	S	30-Oct-10	S	Approved		
82	AEN	Afghan	329531	075148	AEN, 075148, C-IED TF Compound, BAF	10-MCA	4-Jun-10	S	3-Aug-10	S	21-Sep-10	S	5-Nov-10	S	Approved		
83	AES	Afghan	329534	075202	AES, 075202 C2 Facility, Dwyer	10-MCA	3-Aug-10	S	5-Aug-10	S	21-Sep-10	S	5-Nov-10	S	Approved		
84	AES	Afghan	329535	075199	AES, 075199 DFAC, Dwyer	10-MCA	3-Aug-10	S	5-Aug-10	S	21-Sep-10	S	5-Nov-10	S	Approved		
85	AES	Afghan	329590	075200	AES, 075200, Wastewater Treatment Fac, Dwyer	10-MCA	3-Aug-10	S	3-Aug-10	S	21-Sep-10	S	5-Nov-10	S	Approved		
86	AES	Afghan	329635	074129	AES, 074129, Contingency Housing, Ph 5, Kandahar	10-MCA	25-May-10	S	3-Aug-10	S	21-Sep-10	S	5-Nov-10	S	Approved		
87	AES	Afghan	329639	075196	AES, 075196, Wastewater Treatment Facility, Maywand	10-MCA	28-Jul-10	S	3-Aug-10	S	21-Sep-10	S	5-Nov-10	S	Approved		
88	AES	Afghan	329656	075214	AES, 075214, Wastewater Treatment Facility, Tarin Kowt	10-MCA	1-Aug-10	S	3-Aug-10	S	21-Sep-10	S	5-Nov-10	S	Approved		
89	AES	Afghan	329657	075197	AES, 075197, Medical Facility, Role II, Tarin Kowt	10-MCA	29-Jun-10	S	3-Aug-10	S	21-Sep-10	S	5-Nov-10	S	Approved		
90	AES	Afghan	329658	075462	AES, 075462, Rotary Wing Apron, Tombstone/Bastion	10-MCA	3-Aug-10	S	3-Aug-10	S	21-Sep-10	S	5-Nov-10	S	Approved		
91	AES	Afghan	329626	074127	AES, 074127, Contingency Housing, Ph 4, Kandahar	10-MCA	25-May-10	S	3-Aug-10	S	21-Sep-10	S	10-Nov-10	S	Approved		
92	AEN	Afghan	327451	071602	AEN, 071602, CMU Barracks Phase 15-18, BAF	10-MCA	23-Jun-10	S	10-Aug-10	S	28-Sep-10	S	12-Nov-10	S	Approved		
93	AEN	Afghan	329533	074925	AEN, 074925, DFAC, BAF	10-MCA	1-Aug-10	S	10-Aug-10	S	28-Sep-10	S	12-Nov-10	S	Approved		
94	AES	Afghan	329636	074131	AES, 074131, Contingency Housing, Ph 6, Kandahar	10-MCA	25-May-10	S	10-Aug-10	S	28-Sep-10	S	12-Nov-10	S	Approved		
95	AES	Afghan	329637	074132	AES, 074132, Contingency Housing, Ph 7, Kandahar	10-MCA	25-May-10	S	10-Aug-10	S	28-Sep-10	S	12-Nov-10	S	Approved		
96	AES	Afghan	329659	075207	AES, 075207, Contingency Housing (6000 PAX), Tombstone/Bastion	10-MCA	6-Aug-10	S	10-Aug-10	S	28-Sep-10	S	12-Nov-10	S	Approved		
97	AES	Afghan	329285	075560	AES, 075560 Medical Facility, Shindand	10-MCA	9-Jun-10	S	17-Aug-10	S	5-Oct-10	S	19-Nov-10	S	Approved		
98	AES	Afghan	329593	075219	AES, 075219, Waste Mgmt Complex, Frontenac	10-MCA	17-Aug-10	S	23-Aug-10	S	5-Oct-10	S	19-Nov-10	S	Approved		
99	AES	Afghan	329652	075198	AES, 075198, Rotary Wing Apron, Ph 2, Tarin Kowt	10-MCA	8-Jun-10	S	17-Aug-10	S	5-Oct-10	S	19-Nov-10	S	Approved		
100	AES	Afghan	329660	075204	AES, 075204, DFAC (6000 PAX), Tombstone/Bastion	10-MCA	17-Aug-10	S	17-Aug-10	S	5-Oct-10	S	19-Nov-10	S	Approved		
101	AES	Afghan	329592	075213	AES, 075213, Wastewater Treatment Facility, Frontenac	10-MCA	17-Aug-10	S	19-Aug-10	S	7-Oct-10	S	21-Nov-10	S	Approved		
102	AES	Afghan	329661	075206	AES, 075206, Wastewater Treatment Facility, Tombstone/Bastion	10-MCA	24-Aug-10	S	24-Aug-10	S	12-Oct-10	S	26-Nov-10	S	Approved		
103	AEN	Afghan	329525	072606	AEN, 072606 Troop Housing Ph 4, BAF	10-MCA	28-Sep-10	S	2-Oct-10	S	12-Nov-10	S	27-Nov-10	S	Approved		
104	AEN	Afghan	329526	074090	AEN, 074090, Troop Housing Ph 5, BAF	10-MCA	30-Sep-10	S	2-Oct-10	S	12-Nov-10	S	27-Nov-10	S	Approved		
105	AEN	Afghan	329527	074155	AEN, 074155, Troop Housing Ph 6, BAF	10-MCA	30-Sep-10	S	2-Oct-10	S	12-Nov-10	S	27-Nov-10	S	Approved		
106	AEN	Afghan	329528	074157	AEN, 074157, Troop Housing Ph 7, BAF	10-MCA	30-Sep-10	S	2-Oct-10	S	12-Nov-10	S	27-Nov-10	S	Approved		
107	AEN	Afghan	329529	074158	AEN, 074158, Troop Housing Ph 8, BAF	10-MCA	30-Sep-10	S	2-Oct-10	S	12-Nov-10	S	27-Nov-10	S	Approved		
108	AED	Afghan	321924	071488	AEN, 071488 Coalition Operations Center - BAF	10-MCA	30-Aug-10	S	30-Aug-10	S	13-Oct-10	S	30-Nov-10	S	Approved		
109	AEN	Afghan	326247	072477	AEN - 072477, USFOR-A HQ & Housing, Kabul	10-MCA	20-Sep-10	S	5-Oct-10	S	3-Nov-10	S	2-Dec-10	S	Approved		
110	AEN	Afghan	327452	071604	AEN, 071604, Eastside Utilities Infrastructure, BAF	10-MCA	2-Jul-10	S	7-Sep-10	S	26-Oct-10	S	10-Dec-10	S	Approved		
111	AEN	Afghan	327453	071605	AEN, 071605, Eastside Electrical Distribution, BAF	10-MCA	30-Aug-10	S	7-Sep-10	S	26-Oct-10	S	10-Dec-10	S	Approved		

P2 Projects Status Report - FY10 & 11 Pending Awards - AED

Report includes all ACTIVE P2 Projects, including "LCM" status (ie, schedules not yet officially built)

Data Date: 7-Mar-2010 / DD + 45 = 21-Apr-2010

Sorted by Award Date, P2#

Source: OP (Oracle Project)						OP									
#	DIST	INSTL	P2 #	1391	DESCRIPTION	TF	RTA ML180	A S	ADV ML230	A S	OPEN BID ML240	A S	AWARD CC800	A S	P2 Status
112	AEN	Afghan	327455	072242	AEN, 072242, Army Aviation Headquarters Building, BAF	10-MCA	23-Aug-10	S	7-Sep-10	S	26-Oct-10	S	10-Dec-10	S	Approved
113	AEN	Afghan	329532	075509	AEN, 075509, Task Force Freedom Compound, BAF	10-MCA	12-Aug-10	S	7-Sep-10	S	26-Oct-10	S	10-Dec-10	S	Approved
114	AES	Afghan	329662	075195	AES, 075195 Rotary Wing Apron, Ph 2, Wolverine	10-MCA	2-Sep-10	S	7-Sep-10	S	26-Oct-10	S	10-Dec-10	S	Approved
115	AES	Afghan	329664	075194	AES, 075194, Perimeter Fence, Wolverine	10-MCA	30-Aug-10	S	7-Sep-10	S	26-Oct-10	S	10-Dec-10	S	Approved
116	AES	Afghan	329666	075183	AES, 075183, Entry Control Point, Wolverine	10-MCA	30-Aug-10	S	7-Sep-10	S	26-Oct-10	S	10-Dec-10	S	Approved
117	AES	Afghan	329667	075224	AES, 075224, Wastewater Treatment Facility, Wolverine	10-MCA	30-Aug-10	S	7-Sep-10	S	26-Oct-10	S	10-Dec-10	S	Approved
118	AEN	Afghan	327447	068083	AEN, 068083, Consolidated Community Support Area, BAF	10-MCA	9-Sep-10	S	25-Sep-10	S	6-Nov-10	S	16-Dec-10	S	Approved
119	AEN	Afghan	330706	071606	AEN, 071606, Improve Entry Control Point 1, BAF	10-MCA	20-Nov-10	S	21-Nov-10	S	13-Jan-11	S	27-Feb-11	S	Approved
